



BETA Group, Inc.

Engineers • Scientists • Planners

1420 Providence Highway, Suite 117, Norwood, MA 02062 781.255.1982 fax: 781.255.1974
6 Blackstone Valley Place, Lincoln, RI 02865 401.333.2382 fax: 401.333.9225
email: BETA@BETA-eng.com

MEMORANDUM

**City of New Bedford – Keith Middle School
McCoy Field – Env. Contract #2**

August 31, 2004

Subject: Site Walk - August 27, 2004

Project # 02685

To: Sarah Porter, New Bedford ConComm

Cc: Larry Oliveira; Jacqueline Coucci; Al Amaral; Jackie Huggins

From: Al Hanscom

This memorandum has been prepared to document discussions at our site walk on Friday, August 27th and to more fully describe the upcoming work and limits, so that appropriate provisions can be incorporated into an Order of Conditions.

- **Temporary Storage of Topsoil** - WES plans to temporarily store stripped topsoil under the referenced project in the northwest corner of the property, as indicated on the attached sketch (Attachment A). Erosion control fencing and haybales, similar to that used at the edge of the wetlands, will be staked at the base of the pile during the period of storage.
- **Limits of Work** – Due to the presence of waste materials at the surface in the southwest corner of the property, additional remediation of soils will need to be performed under the Special Project Designation issued by DEP. That will necessitate an expansion of the work limits to that illustrated on the attached sketch (Attachment B). Supplemental wetlands delineation has been performed in the area and the updated plan will be presented on Wednesday night.

Note: Both sketches are made on excerpts from Drawing SU1.1 submitted to you earlier this month.

Please call either Evan Warner (508/991-7500) or me at 781/255-1982 with any questions.

Attachment A

4-28-00

DMH#5.3
8' DIA
RIM=92.8
INV1=89.65
INV2=88.45
INV OUT=84.70

Approximate Location
for temporary
storage of
stripped
W-34 topsoil!


CB#5.3.1
RIM=92.5
INV=89.75

Ref. Drawg S11-1
dated 8/06/04

60" DIA. x 100 LF
STORMWATER
DETENTION PIPE
 $S=.0025/FT$

60" DIA.
90d ELBOW
INV=84.46

60" DIA. TEE W/ 24"
RISER, FRAME #

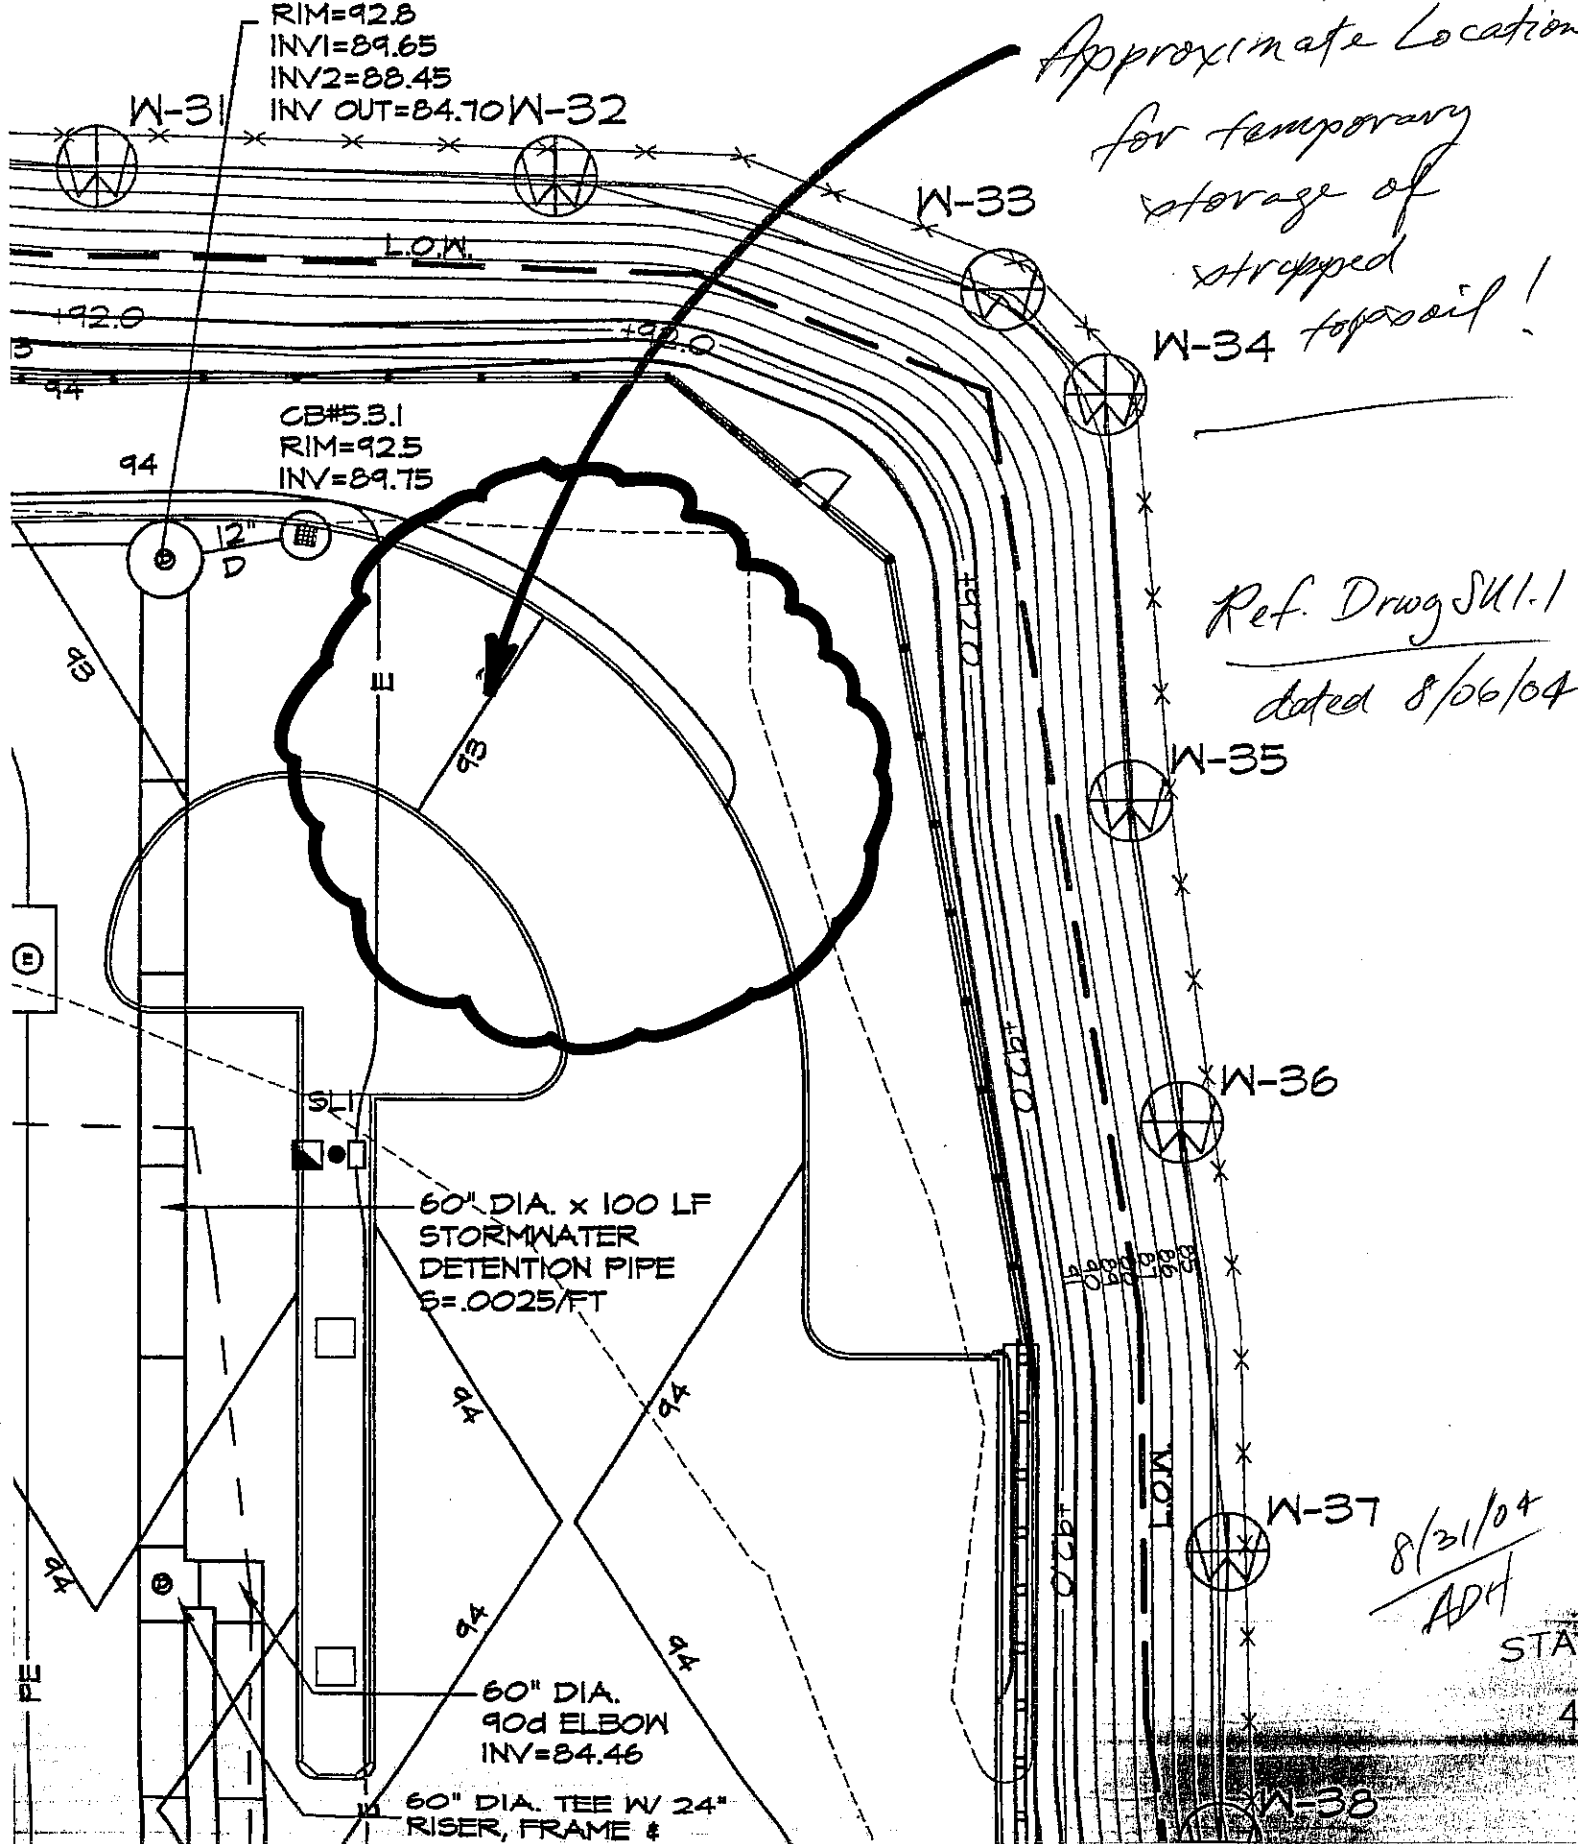

Attachment B

Additional Work
Area at SW
Corner of Site
STANDING WATER

4-28-00

L.O.W.

L.O.W.

SEWER PIPE

Ref. Drwg. SU1.1
dated 8/06/04

60" DIA.
90° ELBOW
W 24"
RISER, 95"
FRAME &
COVER
RIM=95.0
INV=84.98

60" DIA.
MANIFOLD
TEE
INV. 84.96
INV. 84.94

8/31/04
ADK

